



Project Management: Overview

Version SAP Busi10.0ness One

PUBLIC

THE BEST RUN 

- In this training you will find two scenarios that describe some main features of the *Project Management* module.
- An additional training, **Project Management Billing** is also available.
- Please refer to the ***How to Work with Project Management in SAP Business One*** How to Guide document for additional information.

Objectives




At the end of this topic, you will be able to:

- Explain the concept of project management in SAP Business One
- Create, maintain and complete a project using *Project Master Data*
- Connect different objects to a project master data.
- Create and work with subproject
- Monitor your projects using the Gantt chart and project management reports

- At the end of this topic, you will be able to:
 - Explain the concept of project management in SAP Business One
 - Create, maintain and complete a project using Project Master Data
 - Connect different objects to a project master data.
 - Create and work with subproject
 - Monitor your projects using the Gantt chart and project management reports

Concept

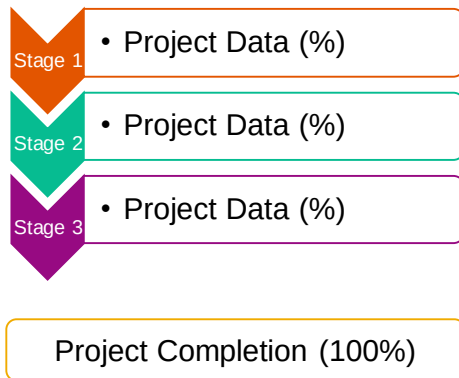


Benefits

- A centralized Project master data enables :
 - Monitoring tasks, progress and general project information
 - Managing project related documents
- A billing wizard enables creating A/R documents in a batch

- The *Project Management* module, enables you to manage different types of projects in the system. The *Project Master Data* window is a workbench that centralizes different aspects of the project and enables you to document the different stages of the project. The list of stages compose the project process and can be used for planning.
- For each stage a progress percentage is defined in a way that all finished project stages will sum up to 100%. Each stage may contain data relevant for that stage of the project. The system analyzes this data to retrieve information about the project value, cost and profit.
- Note that the *Project Management* module should be manually enabled in the *Company Details* window.
- Let us see in the next slide the objects that compose the project data.

Project Data

Project data can be:

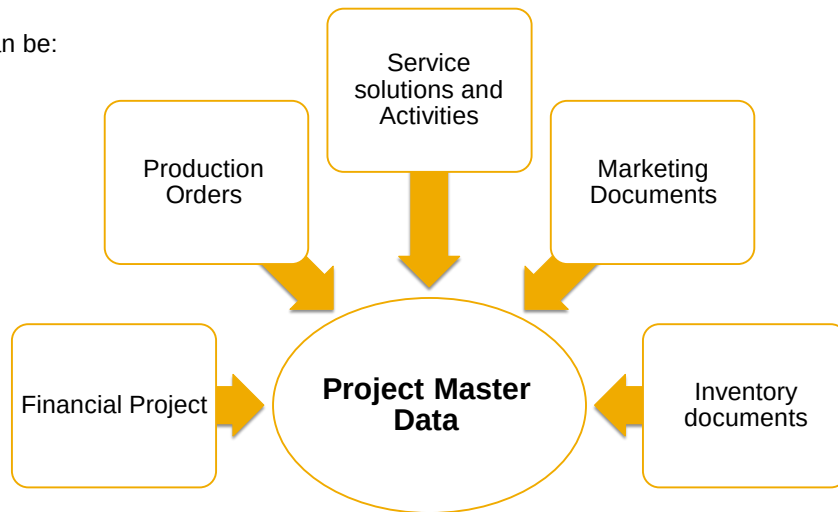


© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

4

For each stage in the *Project Master Data*, different data can be referenced. This data can be composed of marketing and inventory documents, production orders, service solutions and activities. In addition, a financial project code can be linked to each project. The *Project Master Data* forms one entry point for both financial and logistical data.

Project Management Output

Project management output can be:

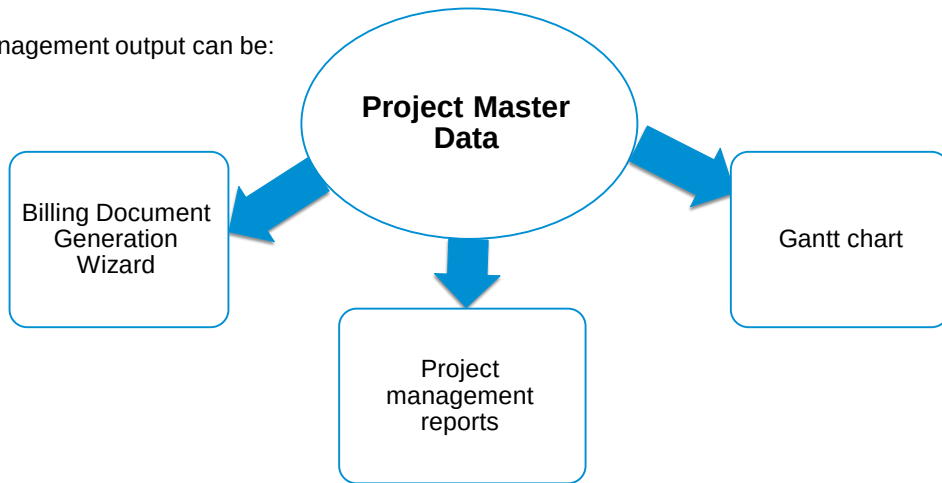

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

5

Using the project information accumulated in the master data, the user can also generate a Gantt chart, reports and run the *Billing Document Generation Wizard* to invoice the project's chargeable costs.

Business Scenario



OEC Computers provide technical IT solutions for their customers. These solutions usually include:

- infrastructure planning and installation,
- providing computer hardware,
- equipment configuration and integration and
- peripheral equipment installation.



OEC computers would like to manage a project for each customer to track the progress of the project according to different milestones.

They would also like to define a budget for the project and analyze its profitability.

In addition, some projects are composed of several subprojects.

To achieve this, OEC computers decide to use the *Project Management* module.

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

6

OEC Computers provide technical IT solutions for their customers. These solutions usually include:

- infrastructure planning and installation,
- providing computer hardware,
- equipment configuration and integration and
- peripheral equipment installation.

OEC computers would like to manage a project for each customer to track the progress of the project according to different milestones.

They would also like to define a budget for the project and analyze its profitability.

In addition, some projects are composed of several subprojects.

To achieve this, OEC computers decide to use the *Project Management* module.

Scenario 1 – The Project Process



© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

7

- In this training we will walk through a project process from the creation step until project completion.
- In the image we can see the different stages of the project in the scenario.
- Note that in many cases, all project stages are created upfront including planned start time and end time of each stage. In our scenario, the stages are created one by one according to the project's progress.

Project Header Information

Project Management → Project Master Data

The screenshot shows the 'Project Master Data' form in SAP. It is divided into two main sections. The left section contains fields for Project Type (radio buttons for External and Internal), BP Code (C20000), BP Name (Maxi-Teq), Contact Person (Norm Thompson), Territory, Sales Employee (Brad Thompson), and Owner. The right section contains fields for Project Name, Project No. (Primary), Status (Started), Start Date (24.09), Due Date, Finished Date, Open Activities (0), % Complete (0%), and a checkbox for Financial Project. Four numbered callouts are present: 1 points to the Project Type field, 2 points to the Status field, 3 points to the % Complete field, and 4 points to the Financial Project checkbox.

- 1 A project performed for a customer is marked as *External* whereas an in-house project is marked as *Internal*.
- 2 Four possible statuses: Started, Paused, Stopped and Finished.
- 3 The complete% progress bar is updated according to the progress percentage of the finished stage rows.
- 4 Connect one financial project in order to link relevant documents associated with this project.

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

8

- Kate is the project manager at OEC Computers. She enters the **Project Master Data** and adds a new project for the customer **Maxi Teq**. A customer project is marked as *External* (1).
- Kate keeps the default status of the project, *Started*, as long as the project is running (2). The different statuses are further explained in the next slides.
- Kate can also track the progress of the project by looking at the *% Complete* field (3). We will also talk about this field in the next slide.
- Finally, Kate links the financial project that was opened by the accountant in the company. This financial project is linked to revenue accounts in the chart of accounts. This way financial information can be tracked for this project and in addition this enables the linkage of relevant documents associated with this project (4). We will see that as well in the next slides.

Project Stages and Completion Progress Rate

The screenshot shows the 'Stages' tab in the SAP Project Master Data interface. It features a table with columns for Start Date, Due Date, Finished Date, Stage, Task, Description, Planned Cost, Invoiced Amount, and a completion percentage. The first stage is 'Conception/Initiation' with two tasks: 'Assign project team' and 'Kick off meeting'. The first task is marked as finished, contributing to a 2% completion rate shown in the '% Complete' field at the top right.

Each finished stage row (task) adds to the progress bar

Predefined project stages that can be edited

Each stage has one or more tasks.

#	Start ...	Due D...	Finished D...	Stage	Task	Description	Planned C...	Invoiced Amoun...	Invoiced Amoun...	%	Finis...
1	24.09	24.09	24.09	Conception/Initiation	Assign project team	Scope, roles and timeline	0.00	0.00	0.00	2.00	☒
2	28.09			Conception/Initiation	Kick off meeting		0.00	0.00	0.00	0.00	☐
3				Conception/Initiation			0.00	0.00	0.00	0.00	☐

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

9

- The **Stages** tab is the backbone of the **Project Master Data**.
- Here you document each stage of the project. Each stage may have more than one task. The list of tasks is common to all stages. This means that each task can be used by different stages.
- In our scenario, Kate defines two tasks for the **Conception/ Initiation** stage. The first is assigning a project team and the second is a kick off meeting.
- Note that stage values can be personalized in a way that fits the company needs.
- The first task is checked as finished and holds **2%** of the project completion. Therefore, the completion progress rate of the entire project is now **2%** as shown in the *% Complete* field.
- Note the difference between the *End Date* and the *Finished Date*. The end date is an estimated or desired date the user enters. The finished date, on the other hand, is the actual date when the stage row was completed. Once checking the *Finished* box, today's date is automatically populated in the *Finished Date* field. This date can be adjusted manually.

Stages Data

Overview		Stages		Summary	Remarks	Attachments	
#	Start ...	Due D...	Finished D...	Stage	Task	Description	Planned C...
1	24.09	24.09	24.09	Conception/Initiation	Assign project team	Scope, roles and timeline	0.00
2	28.09			Conception/Initiation	Kick off meeting		0.00
3				Conception/Initiation			0.00

For each stage row in the upper table, additional data can be added through the options at the bottom

- ▶ Open Issues
- ▶ Attachments
- ▶ Documents
- ▶ Work Orders
- ▶ Activities

- For each stage row, additional data can be entered. After choosing the row of the stage, expand the relevant option to enter the details. The data can be for example an *A/R Invoice* for billing the customer, an *Activity* for a planned meeting or an *Open Issue* that rose during the project process.
- Let us show how we enter this data in the next slides.

Adding an Activity

Overview		Stages		Summary	Remarks	Attachments
#	Start ...	Due D...	Finished D...	Stage	Task	Description
1	24.09.	24.09.	24.09.	Conception/Initiation	Assign project team	Scope, roles and timeline
2	28.09.			Conception/Initiation	Kick off meeting	
3				Conception/Initiation		

A meeting activity was set and connected to the kick off meeting task row

- Open Issues
- Attachments
- Documents
- Work Orders
- ▼ Activities

#	Activity	Type	Start Date	Start Time	End Date	End Time	Assigned To	Remarks
1	31	General	24.09	18:00	24.09	18:15	Jayson Butler	

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

11

- Kate schedules the meeting in a SAP Business One calendar *Activity*. She extends the *Activity* option and from the *Activity* field, she adds a new meeting activity. Relevant information from the activity is copied to the *Activity* row in the project.
- Note that an activity related to a project can be created directly from the CRM or Business Partner module. Once the project data is entered to the activity, it is automatically added to the relevant project stage.
- It is also possible to connect a row stage id from a project in the *Activity* → *Other Details* tab. We will further discuss it later on in the training.

Adding an A/R Invoice

% Complete 7%

#	Start Date	Due D...	Finished D...	Stage	Task	Description	Planned C...	Invoiced Amoun...	Invoiced Amoun...	%	Finis...
1	24.09.	25.09.	24.09.	Conception/Initiation	Assign project team	Scope, roles and timeline	100.00	0.00	0.00	2.00	☒
2	28.09.	28.09.	28.09.	Conception/Initiation	Kick off meeting	Kickoff Meeting	800.00	0.00	0.00	5.00	☒
3	29.09.	12.10.	12.10.	Definition/Planning	Gap Analysis	Gap Analysis	800.00	0.00	0.00	0.00	☐
4	12.10.	12.10.	12.10.	Definition/Planning	Billing	1st Billing	0.00	2,000.00	0.00	0.00	☐
5				Conception/Initiation			0.00	0.00	0.00	0.00	☐

An invoice was issued to the customer and attached to stage row 4

A budgeted cost was entered manually

#	Doc. Type	Doc. No.	Doc. Date	Total	Chargeable
1	A/R Invoice	1313	10.09.	2,000.00	

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

12

- Kate marks the second task as finished and the completion rate now stands on **7%**.
- Then, Kate adds a new stage called **Definition/ Planning** and adds a task for a gap analysis they are about to perform.
- She adds another predefined stage for a monthly billing for the hours invested in this project - **2,000**. After adding the A/R invoice, the amount is copied to the stages table, in the *Invoiced Amount (A/R)* column. This column displays the total amount of all the A/R invoices related to this stage row.
- Kate also manually adds a planned cost for each stage row. This way, a project budget can be planned and compared to the actual accumulated value of the project.
- Note that A/R invoices and deliveries can also be issued in a batch using the *Billing Document Generation* wizard. For more information about the wizard, please refer to the **Project Management – Billing** course topic.

Document Assignment

System Message X

Unassigned documents exist in the system. Do you want to assign them?

Yes No Cancel

1

Document Assignment

Doc. Type	Doc. Nu...	Doc. ...	Date	BP Code	BP Name
A/P Invoice	733	1		V20000	Lasercom
A/P Invoice	734	1		V10000	Acme Associates
A/P Invoice	734	2		V10000	Acme Associates

2

4

Project/Subproject	Name	Stage	D...
▼ Project Stages	▼ Max01		
		▼ 1 - Scope, roles and tim	
		▼ 2 - Kickoff meeting	
		▼ 3 - Gap Analysis meetin	
		▼ 4 - Purchasing and Asse	

3

4

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

13

- Kate adds a fourth stage to the project for the purchasing of hardware and assembling computers and servers.
- Now Kate wants to update the *Project Master Data*. She opens the master data record and a system message pops up as shown in the image. The system recognizes a document that is not connected to the project master data, but has the same financial project code associated with the project – project code **101**. Kate chooses Yes (1) in order to assign the document to the project master data. The Document Assignment window opens. Kate sees an A/P Invoice with several rows. She opens the invoice and realizes this is the equipment purchase invoice for this project. Kate chooses all rows (2), and chooses the relevant stage row, stage 4, on the right side of the window (3). Finally, she chooses the arrow button (4) to relate the document rows.

Managing Documents

Overview											
Stages				Summary		Remarks		Attachments			
#	Start Date	End Date	Finished Date	Stage	Task	Description	Planned Cost	Invoiced Amount (A/R)	Invoiced Amount (A/P)	%	Finished
1	03.09	03.09	03.09	Conception/Initiation	Assign project team	Scope, roles and time line	100.00	0.00	0.00	2.00	☒
2	05.09	05.09	05.09	Conception/Initiation	Kick off meeting	Kickoff meeting	800.00	0.00	0.00	5.00	☒
3	06.09	18.10	17.10	Definition/Planning	Gap Analysis	Gap Analysis	800.00	0.00	0.00	0.00	☐
4	18.09	18.09	18.09	Definition/Planning	Billing	1st billing	0.00	2,000.00	0.00	0.00	☐
5	29.09	15.10	16.10	Launch/Execution	Purchasing and Asse	Purchasing and assembly	50,000.00	0.00	0.00	0.00	☐
6	16.10	16.10		Conception/Initiation	Billing	2nd billing	0.00	29,000.00	0.00	0.00	☐
7				Conception/Initiation			0.00	0.00	0.00	0.00	☐

► Open Issues

► Attachments

▼ Documents

#	Doc. Type	Doc. No.	Doc. Date
1	A/P Invoice	733	28.08.18
2	A/P Invoice	734	12.09.18
3	A/P Invoice	734	12.09.18

- In the image we see the *Documents* section is extended for the 6th stage row. There we can see the A/P invoice row that was related to the *Project Master Data* in the previous step. Kate also attaches the vendor's scanned invoice in the *Attachment* tab. The total amount of the A/P Invoice now appears in the *Invoiced Amount (A/P)* column for stage 4.
- Note that any document can also be added manually in the *Document* section.

Connecting a Project Stage in Documents

Project Type ☒ External ☐ Internal

Project Name

BP Code

Project No.

BP Name

Status

...

Overview Stages Summary Remarks Attachments

Position	Start Date	End Date	Stage	Task	Description	Unique ID	...
1			Conception	Assign team	Scope	Con1	
2			Conception	Kickoff meeting	Meeting	Con2	

A project can be manually connected using the *Stage* field in:

- Marketing documents
- Time sheet
- Activities

Time Sheet

Type

ID

Name

First Name

#	Date	Start time	End Time	Stage
1	25.9.18	09:00	18:00	Con1(6-1) *

* The value 6 is the internal key of the project

- We already saw the possibility to connect a document in a *Project Master Data* but it is also possible to connect a project's stage row to a document row. This connection is done in the *Stage* column.
- The *Stage* value is the concatenation of the project (the internal key) and stage row numbers, and the *Unique ID* field in the stage row (if defined).
- The *Unique ID* in the project master data is a free text and optional field that the user can fill in for each stage row. Then, in marketing documents, *Activities* and the *Time Sheet*, this unique ID can be used to identify and connect these documents to a project's stage. It is recommended to give a meaningful name to the unique ID field to easily find it in the list of IDs.
- Note that connecting a project stage in a document row is possible only when the same financial project code is connected to the project master data and to the document row.
- The time sheet topic is covered in the **Project Management Billing** course.

Managing Production Orders in a Stage



- ▶ Open Issues
- ▶ Attachments
- ▶ Documents
- ▼ Work Orders

#	Doc. No.	Description	Status	Planned Qty	Due Date	Days Overdue	Type	No.	Description	Base Qty	Planned Qty	Issued	Additional Qty	Available	UoM Name
1	855	Server Point 10000	Planned	1.000000	30.09.18	0									
2							Item	A00001	J.B. Officeprint 1420	1.000	1.000	0.000	0.000	242.000	
3							Item	P10001	PC - P4 2.4G, DDR 512M, 400G HD	1.000	1.000	0.000	0.000	-39.000	
4							Item	L10001	Labour	1.000	1.000	0.000	0.000	0.000	
5															

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

16

- OEC Computers assembled a server in a production process for this project. Kate opens the *Work Order* section, of the 4th stage, and adds the relevant *Production Order* as shown in the lower image. Only *Production Orders* with the same financial project code are shown in the list to choose from. Alternatively, we can manually add a new *Production Order* directly, without indicating a financial project code.
- In the *Production Order* we can add resources for the employees involved in this project. This way, the project can reflect the employee cost and also allows managing the employee capacity.

Stage Row Dependency

Overview									
Stages									
Summary									
Remarks									
Attachments									
#	Start Date	End Date	Finished Date	Stage	Task	Description	Planned Cost	%	Finished
1	03.09	03.09	03.09	Conception/Initiation	Assign project team	Scope, roles and time line	100.00	2.00	☒
2	05.09	05.09	05.09	Conception/Initiation	Kick off meeting	Kickoff meeting	800.00	5.00	☒
3	06.09	18.10	17.10	Definition/Planning	Gap Analysis	Gap Analysis	800.00	0.00	☒
4	18.09	18.09	18.09	Definition/Planning	Billing	1st billing	0.00	0.00	☒
5	29.09	15.10	16.10	Launch/Execution	Purchasing and Asse	Purchasing and assembly	50,000.00	0.00	☒
6	16.10	16.10		Conception/Initiation	Billing	2nd billing	0.00	0.00	☐
7				Conception/Initiation			0.00	0.00	☐

- You can define up to 4 different dependencies.
- When a stage row is dependent on another task, it can be marked as finished as long as the base task is finished as well.

- In our project, stage row 5, **Purchasing and Assembly**, is dependent on stage row 3, **Gap Analysis**. This means that only after Kate marks task 3 as finished can she mark task 5 as finished as well. The reason Kate creates this dependency is to make sure that all preparations made in this stage align with all the recommendations of the gap analysis.
- It is also possible to add a dependency on a stage from a different subproject. We will learn about subprojects later on in this training.

Handling Open Issues in a Project

Overview										
Stages			Summary		Remarks	Attachments				
#	Start Date	End Date	Finished Date	Stage	Task	Description	Planned Cost	%	Finished	Stage Dependence (1)
1	03.09.	03.09.	03.09.	Conception/Initiation	Assign project team	Scope, roles and time line	100.00	2.00	☒	
2	05.09.	05.09.	05.09.	Conception/Initiation	Kick off meeting	Kickoff meeting	800.00	5.00	☒	
3	06.09.	18.10.	17.10.	Definition/Planning	Gap Analysis	Gap Analysis	800.00	10.00	☒	
4	18.09.	18.09.	18.09.	Definition/Planning	Billing	1st billing	0.00	0.00	☒	
5	29.09.	15.10.	16.10.	Launch/Execution	Purchasing and Asse	Purchasing and assembly	50,000.00	30.00	☒	Gap Analysis
6	16.10.	16.10.	16.10.	Launch/Execution	Billing	2nd billing	0.00	0.00	☐	
7	20.10.	25.10.		Launch/Execution	Configuration	configuration	0.00	0.00	☐	
8				Conception/Initiation			0.00	0.00	☐	

During the configuration stage (Stage row 7) an issue occurred concerning manufacture certification creation.

Open Issues									
#	Area	Priority	Remarks	Closed	Solution	Solution Description	Responsible	Entered By	Date Entered
1	Manufacture	High		☒	27	ABC manufacture certification		Sideton, Kate	

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

18

- The time for equipment installation at the customer site has arrived and Kate adds stage row **7** for **Configuration and Integration**.
- During installation, the technician on site encounters a problem concerning a certification needed for a certain software installation. The technician calls Kate and asks for her help. Kate creates an *Open Issue* record for Stage row **7** and looks for a pre-defined solution from the solution knowledge base in the *Solution* column of the *Open Issue* section. This is the same solution knowledge base from the Service module. Kate finds solution No. **27** with the relevant certification information and calls the technician on site. Once the issue is solved, Kate marks the issue as closed.
- Note that a stage row cannot be marked as finished while an open issue related to this stage exists.
- Also note that the solution knowledge base is defined in the Service module.
- An open-issues dedicated report exists to analyze recurring issues in projects. This way management can track bottle necks or spot issues that can be predicted and better managed.

Stage Owner

Overview Stages Summary Remarks Attachments										
#	Start Date	End Date	Finished Date	Stage	Task	Description	Planned Cost	%	Finished	Owner
1	03.09.	03.09.	03.09.	Conception/Initiation	Assign project team	Scope, roles and time line	100.00	2.00	☒	
2	05.09.	05.09.	05.09.	Conception/Initiation	Kick off meeting	Kickoff meeting	800.00	5.00	☒	
3	06.09.	18.10.	17.10.	Definition/Planning	Gap Analysis	Gap Analysis	800.00	10.00	☒	
4	18.09.	18.09.	18.09.	Definition/Planning	Billing	1st billing	0.00	0.00	☒	
5	29.09.	15.10.	16.10.	Launch/Execution	Purchasing and Asse	Purchasing and assembly	50,000.00	30.00	☒	
6	16.10.	16.10.	16.10.	Launch/Execution	Billing	2nd billing	0.00	0.00	☒	
7	20.10.	25.10.	25.10.	Launch/Execution	Configuration	configuration	0.00	23.00	☐	➡ Milton, Kate
8	25.10.			Finishing Stage	Pilot and sign off	Pilot and sign off	0.00	0.00	☐	
9				Conception/Initiation			0.00	0.00	☐	

- The last stage of the project has arrived: running a pilot and signing off the project. This time Kate assigns herself, as the owner of this stage row. She is responsible at the customer site to run the pilot and handle rejections.

Project Summary 1/2

Budget

Budget	51,700.00
Open Amount (A/P)	0.00
Invoiced (A/P)	35,000.00
Total (A/P)	35,000.00
Total Variance	-16,700.00
Variance %	-32.30

Profit Values

Potential Amount	50,000.00
Open Amount	0.00
Invoiced (A/R)	31,000.00
Total (A/R)	31,000.00
Total Variance	-29,000.00
Variance %	-48.33

Work Order Costs

Actual Item Component Cost	0.00
Actual Resource Component Cost	0.00
Actual Additional Cost	0.00
Actual Product Cost	0.00
Actual By-Product Cost	0.00
Total Variance	0.00

Accumulated Budget

Accumulated Budget	51,700.00
Accumulated Open Amount (A/P)	0.00
Accumulated Invoiced (A/P)	35,000.00
Accumulated Total (A/P)	35,000.00
Accumulated Total Variance	-16,700.00
Variance %	-32.30

Accumulated Profit Values

Accumulated Potential Amount	60,000.00
Accumulated Open Amount (A/R)	0.00
Accumulated Invoiced (A/R)	31,000.00
Accumulated Total (A/R)	31,000.00
Accumulated Total Variance	-29,000.00
Variance %	-48.33

Dates

Due Date	
Actual Closing Date	
Overdue	0

Planned Cost

Planned Cost	100.00
Planned Cost	800.00
Planned Cost	800.00
Planned Cost	0.00
Planned Cost	50,000.00
Planned Cost	0.00

Relevant when working with sub-projects

Total Variance = Total A/P - Budget

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

20

- The *Summary* tab provides important information like: planned cost (budget) vs. actual stage value, profit parameters and production and resources costs.
- In the image, the highlighted section at the bottom is relevant when working with sub-projects and shows the total amounts of all sub-projects. The data at the top of the window is relevant for the current project/subproject. The project in the image, has no subprojects and therefore the data at the bottom is equal to the data in the upper section.
- In the *Budget* section, the subproject Budget field is actually the total *Planned Cost* column amounts of all the stage rows (as appears in the *Stages* tab). The *Total Variance* value is a calculation of the *Total A/P* field value – (minus) the *Budget*. In the *Variance %* field, we see that the actual cost of AP document is **32%** less than the planned cost.
- Note that the *Open Amount (A/P)* field value is the total of all open A/P documents connected to this project/subproject excluding the A/P invoice. This allows better planning upcoming project expenses.

Project Summary 2/2

Expected income → manually entered

Total Variance =
Total A/R – Potential amount

Relevant when working with sub-projects


Overview	Stages	Summary	Remarks	Attachments																																										
<table border="1"> <tr> <td colspan="2">Budget</td> <td colspan="2">Profit Values</td> <td colspan="2">Work Order Costs</td> </tr> <tr> <td>Budget</td> <td>51,700.00</td> <td>Potential Amount</td> <td>60,000.00</td> <td>Actual Item Component Cost</td> <td>0.00</td> </tr> <tr> <td>Open Amount (A/P)</td> <td>0.00</td> <td>Open Amount (A/R)</td> <td>0.00</td> <td>Actual Resource Component Cost</td> <td>0.00</td> </tr> <tr> <td>Invoiced (A/P)</td> <td>35,000.00</td> <td>Invoiced (A/R)</td> <td>31,000.00</td> <td>Actual Additional Cost</td> <td>0.00</td> </tr> <tr> <td>Total (A/P)</td> <td>35,000.00</td> <td>Total (A/R)</td> <td>31,000.00</td> <td>Actual Product Cost</td> <td>0.00</td> </tr> <tr> <td>Total Variance</td> <td>-16,700.00</td> <td>Total Variance</td> <td>-29,000.00</td> <td>Actual By-Product Cost</td> <td>0.00</td> </tr> <tr> <td>Variance %</td> <td>-32.30</td> <td>Variance %</td> <td>-48.33</td> <td>Total Variance</td> <td>0.00</td> </tr> </table>					Budget		Profit Values		Work Order Costs		Budget	51,700.00	Potential Amount	60,000.00	Actual Item Component Cost	0.00	Open Amount (A/P)	0.00	Open Amount (A/R)	0.00	Actual Resource Component Cost	0.00	Invoiced (A/P)	35,000.00	Invoiced (A/R)	31,000.00	Actual Additional Cost	0.00	Total (A/P)	35,000.00	Total (A/R)	31,000.00	Actual Product Cost	0.00	Total Variance	-16,700.00	Total Variance	-29,000.00	Actual By-Product Cost	0.00	Variance %	-32.30	Variance %	-48.33	Total Variance	0.00
Budget		Profit Values		Work Order Costs																																										
Budget	51,700.00	Potential Amount	60,000.00	Actual Item Component Cost	0.00																																									
Open Amount (A/P)	0.00	Open Amount (A/R)	0.00	Actual Resource Component Cost	0.00																																									
Invoiced (A/P)	35,000.00	Invoiced (A/R)	31,000.00	Actual Additional Cost	0.00																																									
Total (A/P)	35,000.00	Total (A/R)	31,000.00	Actual Product Cost	0.00																																									
Total Variance	-16,700.00	Total Variance	-29,000.00	Actual By-Product Cost	0.00																																									
Variance %	-32.30	Variance %	-48.33	Total Variance	0.00																																									
<table border="1"> <tr> <td colspan="2">Accumulated Budget</td> <td colspan="2">Accumulated Profit Values</td> <td colspan="2">Accumulated Work Order Costs</td> </tr> <tr> <td>Accumulated Budget</td> <td>51,700.00</td> <td>Accumulated Potential Amount</td> <td>60,000.00</td> <td>Due Date</td> <td></td> </tr> <tr> <td>Accumulated Open Amount (A/P)</td> <td>0.00</td> <td>Accumulated Open Amount (A/R)</td> <td>0.00</td> <td>Actual Closing Date</td> <td></td> </tr> <tr> <td>Accumulated Invoiced (A/P)</td> <td>35,000.00</td> <td>Accumulated Invoiced (A/R)</td> <td>31,000.00</td> <td>Overdue</td> <td>0</td> </tr> <tr> <td>Accumulated Total (A/P)</td> <td>35,000.00</td> <td>Accumulated Total (A/R)</td> <td>31,000.00</td> <td></td> <td></td> </tr> <tr> <td>Accumulated Total Variance</td> <td>-16,700.00</td> <td>Accumulated Total Variance</td> <td>-29,000.00</td> <td></td> <td></td> </tr> <tr> <td>Variance %</td> <td>-32.30</td> <td>Variance %</td> <td>-48.33</td> <td></td> <td></td> </tr> </table>					Accumulated Budget		Accumulated Profit Values		Accumulated Work Order Costs		Accumulated Budget	51,700.00	Accumulated Potential Amount	60,000.00	Due Date		Accumulated Open Amount (A/P)	0.00	Accumulated Open Amount (A/R)	0.00	Actual Closing Date		Accumulated Invoiced (A/P)	35,000.00	Accumulated Invoiced (A/R)	31,000.00	Overdue	0	Accumulated Total (A/P)	35,000.00	Accumulated Total (A/R)	31,000.00			Accumulated Total Variance	-16,700.00	Accumulated Total Variance	-29,000.00			Variance %	-32.30	Variance %	-48.33		
Accumulated Budget		Accumulated Profit Values		Accumulated Work Order Costs																																										
Accumulated Budget	51,700.00	Accumulated Potential Amount	60,000.00	Due Date																																										
Accumulated Open Amount (A/P)	0.00	Accumulated Open Amount (A/R)	0.00	Actual Closing Date																																										
Accumulated Invoiced (A/P)	35,000.00	Accumulated Invoiced (A/R)	31,000.00	Overdue	0																																									
Accumulated Total (A/P)	35,000.00	Accumulated Total (A/R)	31,000.00																																											
Accumulated Total Variance	-16,700.00	Accumulated Total Variance	-29,000.00																																											
Variance %	-32.30	Variance %	-48.33																																											

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

21

- In the Profit Values section, we see income data. Kate manually entered the expected income amount from this project. Then she saw that the total customer invoiced amount did not reach yet the expected amount. Kate expects that this gap will be eliminated in the next billing round. The *Open Amount (A/R)* field shows all open A/R documents except for A/R invoices.
- In the *Work Order Costs* section we see the different production related costs. Note that the *Total Variance* amount is the sum of all the *Production Orders Variance Total* amounts (as indicated in the production order summary tab), related to this project.

Project Status

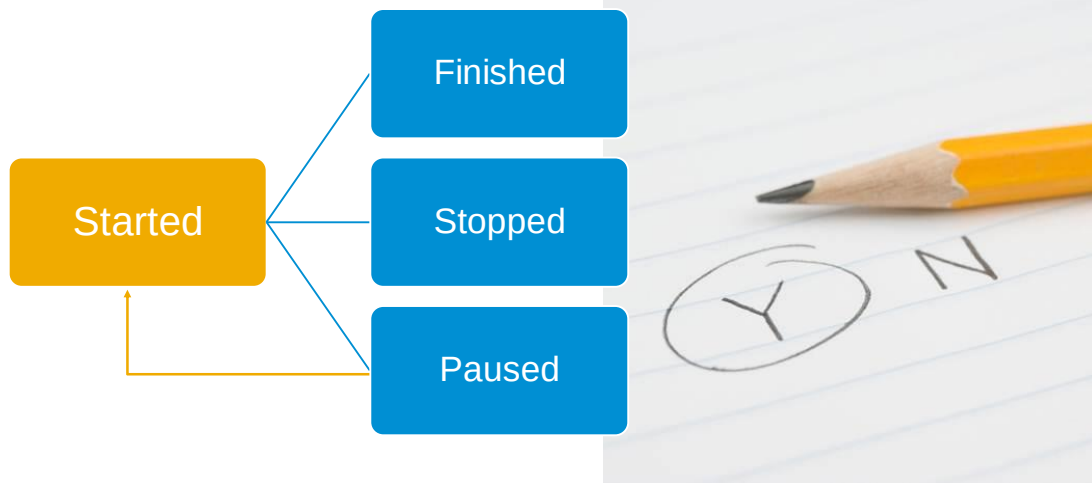

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

22

- When a project is done and all obligations to the customer are fulfilled, Kate changes the status of the project from *Started* to *Finished*.
- To finish a project all tasks should be checked as *Finished*
- There are two other status values that Kate did not use in this project. The first is status *Stopped*. Kate chooses this status when a project is stopped before anticipated.
- When selecting *Stopped* or *Finished*, the current date is automatically updated in the closing date field but can be changed.
- To put a project on hold temporarily, the *Paused* status should be chosen.

Scenario 2 - Working with Subprojects

Project – Parameter100

Project Type ☒ External ☐ Internal **Project Name** Parameter100

BP Code C2000 **Project No.** 5

BP Name Parameter Technologies **Status** Started ▼

Project with Subprojects

Overview Subprojects Stages Summary Remarks Attachments

	Subproject	Start Date	End Date	Planned Cost	Completeness%		
1	London	01.10	31.10	35000	20		
2	Cambridge	15.10	15.11	25000			

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

23

The subproject feature enables managing complex projects where each subproject has its own stages and summary data. A subproject may contain further subprojects underneath it, thus forming a hierarchical tree of subprojects, with the main project at the top level. Kate manages another project for a big customer – **Parameter Technologies**. This customer has several locations and need to renew IT equipment and infrastructure in all their locations. Kate decides to create a subproject for each location. This way she can manage the project data for each location but also manage accumulated data from all the locations.

Adding and Duplicating Subprojects

The screenshot shows the 'Subproject – London [Project: Parameter100]' dialog box. It contains fields for 'Subproject' (London), 'Parent Project/Subproject No.' (5), 'Subproject contribution %' (20), 'Status' (Open), 'Start Date' (01.10.), and 'End Date'. Below these fields are three buttons: 'OK', 'Cancel', and 'Add New Subproject'. The 'Add New Subproject' button is highlighted with a yellow box, and a yellow arrow points from it to a 'List of Subproject' table. The table has the following rows: 'London', 'Phase1', 'Phase2', and '...'. The 'London' row is highlighted with a yellow box.

Subproject – London [Project: Parameter100]	
Subproject	London
Parent Project/Subproject No.	5
Subproject contribution %	20
...	
Status	Open
Start Date	01.10.
End Date	
...	
List of Subproject	
London	
Phase1	
Phase2	
...	
Add New Subproject	
OK	Cancel

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

24

Kate creates subproject **London** underneath project **Parameter100**. Then before adding a second subproject she realized all subprojects are similar. Therefore Kate decides to duplicate subproject **London**, that she already created. She chooses the option to add sub project from template, as shown in the image, and then chooses **London** from the *List of Subprojects*.

Subproject Contribution

Subproject – London [Project: Parameter100]

Subproject	London	Status	Open
Parent Project/Subproject No.	5	Start Date	01.10.18
Subproject Contribution %	20	End Date	
...		...	
		Completeness%	50%

Project – Parameter100

Project Type	☒ External ☐ Internal	Project Name	Parameter100
BP Code	C2000	Project No.	5
BP Name	Parameter Technologies	...	
...		Completeness%	10%

Dashed arrows indicate the calculation: 20% (Subproject Contribution %) * 50% (Subproject Completeness%) = 10% (Project Completeness%).

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

25

*In each subproject, Kate defines the relative portion of the subproject from the entire project by entering a percentage in the **Contribution %** field.*

Look at the image. Subproject **London** is defined as **20%** out of project **Parameter100**. We can also see in the image that it is **50%** completed.

Since other subprojects have not started yet, the *completeness%* of the entire project is **10%** which is **50%** out of **20%** defined for subproject **London**.

Overview of a Project

A project overview can be seen in:

- The *Overview* tab
- The *Project Overview* report generated from the context menu in the *Project Master Data*

Choose *Project Overview*
from the context menu

Project - Parameter100

Project Type

BP Code

BP Name

Contact Person

Territory

Sales Employee

Owner

☒ External
 ☐ Internal

C00000

Maxi-Teq

Norm Thompson

Sales Manager

☒ Project with Subprojects

Overview

Subprojects

Stages

Summary

Remarks

Attachments

Risk Level

Industry

Comments

Low

Subprojects	Fulfillment	Status
1 London	% 50.00	Open
2 Cambridge	% 0.00	Open
3 Cardiff	% 0.00	Open


Project

Select Level 2

Project / Subproject	Stage	Task	Start Date	Due Date
Parameter100			03.10	
London			03.10	
	Definition/Planning	Planning	03.10	05.10
	Definition/Planning	Purchasing and Assembly	05.10	05.11
	Launch/Execution	Installation	05.11	15.11
	Finishing Stage	Testing	15.11	15.11
Cambridge			03.10	
	Definition/Planning	Planning	08.10	10.10
	Definition/Planning	Purchasing and Assembly	10.10	10.11
	Launch/Execution	Installation	10.11	20.11
	Finishing Stage	Testing	20.11	20.11
Cardiff			03.10	
	Definition/Planning	Planning	13.10	15.10
	Definition/Planning	Purchasing and Assembly	15.10	15.11

Kate added several subprojects according to the different locations in project **Parameter100**. Now she goes to the *Overview* tab to receive a wider view of all her subprojects. She also opens the *Project Overview* from the context menu of the *Project Master Data*. The project overview works as a workbench where Kate can view the different subprojects progress, mark a stage row as completed and open each subproject master data in the list.

Gantt Chart

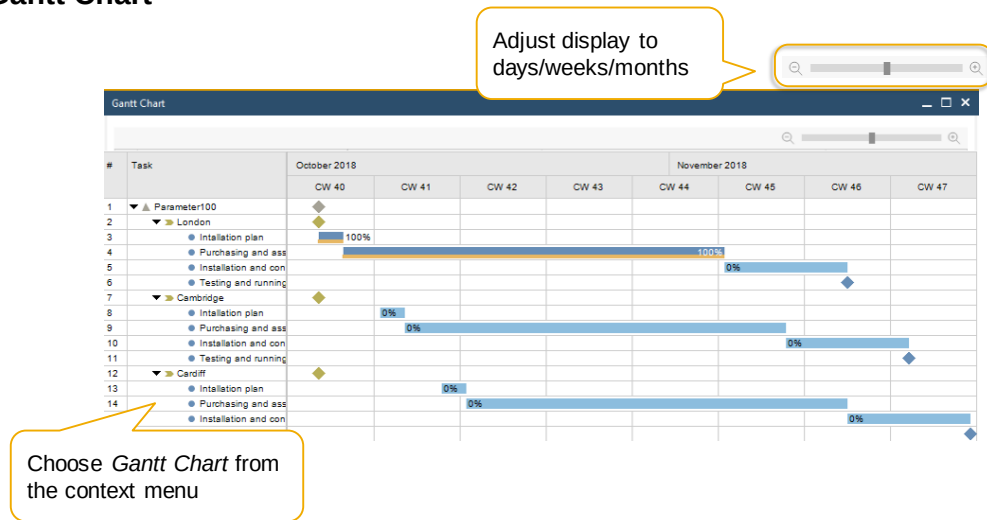


© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

27

Another way to monitor a project is by viewing its Gantt chart. You do that by choosing *Gantt Chart* from the context menu of the *Project Master Data*. Look at the image. You can see 3 subprojects for project **Parameter100**. Each subproject has the same structure with identical 4 stage rows. However, each subproject starts and ends in different dates. You can move Gantt Chart time bars of subprojects and project stages to update project timelines for planning purposes.

Project Reports

Three available reports:

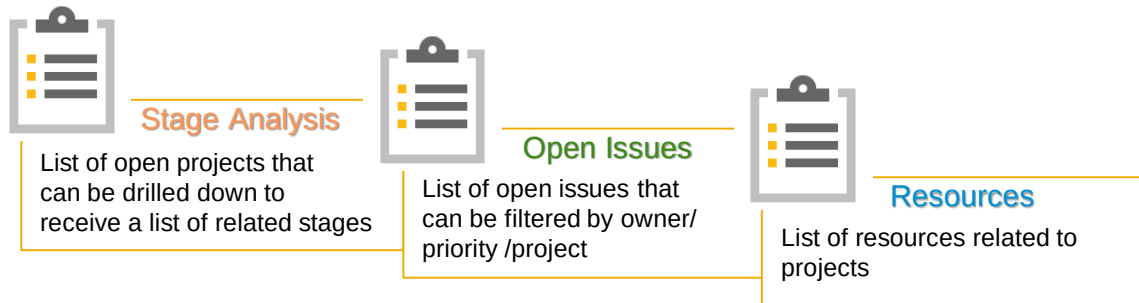

© 2020 SAP SE or an SAP affiliate company. All rights reserved. | INTERNAL

28

- There are 3 different reports in the *Project* module as shown in the image. These reports can analyze multiple projects and give a cross project overview.
- Kate uses the *Stage Analysis* report to receive the full list of open projects and stages. This report is a monitoring tool that provides different project data.
- To monitor statistics of high occurrence of specific open issues, Kate runs the *Open Issues* report.
- In addition, she uses the *Resources* report to track technicians (that are defined as resources in Production Orders).
- These reports can be very helpful when working with sub-projects as well since this way the project data is grouped together in the reports.
- Note there is a forth report that provides an overview of the time sheet records related to projects. Refer to the **Project Management Billing** course to learn more about the time sheet.

Summary 1/2



Here are some key points:

- A project is composed of stages.
- Each row in the *Stages* tab represents a certain task in a stage. Several tasks (rows) can be defined for one stage.
- Each stage row holds a completion rate.
The completion rates of all stages amount to 100%.
- We can relate, for each stage row, different kinds of data including: documents, production orders, activities, open issues (incidents) and attachments.
- The system recommends assignment of documents to a project according to the related financial project code.
- It is also possible to connect stage rows within marketing documents, *Activities* and the *Time Sheet* by choosing the stage id in the document's rows.

Here are some key points:

- A project is composed of stages.
- Each row in the *Stages* tab represents a certain task in a stage. Several tasks (rows) can be defined for one stage.
- Each stage row holds a completion rate.
The completion rates of all stages amount to 100%.
- We can relate, for each stage row, different kinds of data including: documents, production orders, activities, open issues (incidents) and attachments.
- The system recommends assignment of documents to a project according to the related financial project code.
- It is also possible to connect stage rows within marketing documents, *Activities* and the *Time Sheet* by choosing the stage id in the document's rows.

Summary 2/2



- When a financial project exists, it is important to link it to the project master data, in order to enable document assignment and to relate production documents.
- We can set a stage row to be dependent on the completion of another stage row. A dependency can be defined between stages of different subprojects as well.
- In the *Summary* tab we can find useful project information like project profit, budget and cost. Accumulated sub-project information is also displayed in the *Summary* tab.
- A project can have subprojects underneath it. Each subproject can have its own subprojects and so on, forming an hierarchical structure of subprojects where the project is at the top level.
- For each subproject, a contribution % should be defined to determine the portion of the subproject from the main project. This portion determines the relative contribution to the main project completeness.
- When working with several subproject it is helpful to view the entire project in the project overview and the *Gantt* chart.

- When a financial project exists, it is important to link it to the project master data, in order to enable document assignment and to relate production documents.
- We can set a stage row to be dependent on the completion of another stage row. A dependency can be defined between stages of different subprojects as well.
- In the *Summary* tab we can find useful project information like project profit, budget and cost. Accumulated sub-project information is also displayed in the *Summary* tab.
- A project can have subprojects underneath it. Each subproject can have its own subprojects and so on, forming an hierarchical structure of subprojects where the project is at the top level.
- For each subproject, a contribution % should be defined to determine the portion of the subproject from the main project. This portion determines the relative contribution to the main project completeness.
- When working with several subproject it is helpful to view the entire project in the project overview and the *Gantt* chart.

© 2020 SAP SE or an SAP affiliate company. All rights reserved.

No part of this publication may be reproduced or transmitted in any form or for any purpose without the express permission of SAP SE or an SAP affiliate company.

The information contained herein may be changed without prior notice. Some software products marketed by SAP SE and its distributors contain proprietary software components of other software vendors. National product specifications may vary.

These materials are provided by SAP SE or an SAP affiliate company for informational purposes only, without representation or warranty of any kind, and SAP or its affiliated companies shall not be liable for errors or omissions with respect to the materials. The only warranties for SAP or SAP affiliate company products and services are those that are set forth in the express warranty statements accompanying such products and services, if any. Nothing herein should be construed as constituting an additional warranty.

In particular, SAP SE or its affiliated companies have no obligation to pursue any course of business outlined in this document or any related presentation, or to develop or release any functionality mentioned therein. This document, or any related presentation, and SAP SE's or its affiliated companies' strategy and possible future developments, products, and platforms, directions, and functionality are all subject to change and may be changed by SAP SE or its affiliated companies at any time for any reason without notice. The information in this document is not a commitment, promise, or legal obligation to deliver any material, code, or functionality. All forward-looking statements are subject to various risks and uncertainties that could cause actual results to differ materially from expectations. Readers are cautioned not to place undue reliance on these forward-looking statements, and they should not be relied upon in making purchasing decisions.

SAP and other SAP products and services mentioned herein as well as their respective logos are trademarks or registered trademarks of SAP SE (or an SAP affiliate company) in Germany and other countries. All other product and service names mentioned are the trademarks of their respective companies.

See <http://global.sap.com/corporate-en/legal/copyright/index.epx> for additional trademark information and notices.
